

AREO WESTBOW ROUNDABOUT

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	8, '19	May 5, '19	May 12, '19	May 19,																	
								M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S
1																												
2		GENERAL CONDITIONS	20 days	Mon 4/8/19	Fri 5/3/19																							
3		SUBMITTALS	20 days	Mon 4/8/19	Fri 5/3/19																							
4		ELECTRICAL	15 days	Mon 4/8/19	Fri 4/26/19																							
5		PCCP	5 days	Mon 4/29/19	Fri 5/3/19																							
6		GRADING AND PIPE	5 days	Mon 4/29/19	Fri 5/3/19																							
7		CURB AND SIDEWALK	5 days	Mon 4/29/19	Fri 5/3/19																							
8		SIGNS AND STRIPING	5 days	Mon 4/29/19	Fri 5/3/19																							
9		TRAFFIC CONTROL	6 days	Mon 4/29/19	Mon 5/6/19																							
10		7 DAY NOTIFICATION	5 days	Mon 4/29/19	Fri 5/3/19																							
11		SWITCH TRAFFIC TO PHASE 1	1 day	Mon 5/6/19	Mon 5/6/19	10																						
12		FINAL CLEANUP	4 days	Tue 8/27/19	Fri 8/30/19																							
13		ACME FINAL CLEANUP	4 days	Tue 8/27/19	Fri 8/30/19	71,72,68,69																						
14		PROJECT COMPLETE	0 days	Mon 9/2/19	Mon 9/2/19	13																						
15		PHASE 1	22 days	Mon 5/6/19	Tue 6/4/19																							
16		ACME	21 days	Mon 5/6/19	Mon 6/3/19																							
17		SAW CUT AND BREAK PCCP	1 day	Mon 5/6/19	Mon 5/6/19	10																						
18		PCCP	5 days	Tue 5/28/19	Mon 6/3/19	28																						
19		MURPHY BROTHERS	13 days	Tue 5/7/19	Thu 5/23/19																							
20		REMOVE PCCP, SIDWALK, CURB	2 days	Tue 5/7/19	Wed 5/8/19	17																						
21		EXCAVATON AND EMBANKMENT	4 days	Thu 5/9/19	Tue 5/14/19	20																						
22		DRAINAGE	2 days	Wed 5/15/19	Thu 5/16/19	21																						
23		FINISH SUB GRADE	1 day	Fri 5/17/19	Fri 5/17/19	22																						
24		CSBC	2 days	Wed 5/22/19	Thu 5/23/19	23,26																						
25		POWER CITY	5 days	Wed 5/15/19	Tue 5/21/19																							
26		ELECTRICAL	5 days	Wed 5/15/19	Tue 5/21/19	21																						
27		FIVE STAR	2 days	Fri 5/24/19	Mon 5/27/19																							
28		CURB AND SIDEWALK	2 days	Fri 5/24/19	Mon 5/27/19	24																						
29		STRIPE RITE	1 day	Tue 6/4/19	Tue 6/4/19																							
30		TEMP STRIPE FOR PHASE 2	1 day	Tue 6/4/19	Tue 6/4/19	18																						
31		PHASE 2	34 days?	Wed 6/5/19	Mon 7/22/19																							
32		ACME	23 days	Wed 6/5/19	Fri 7/5/19																							
33		SAW CUT AND BREAK PCCP	2 days	Wed 6/5/19	Thu 6/6/19	30																						
34		PCCP	5 days	Mon 7/1/19	Fri 7/5/19	44																						
35		MURPHY BROTHERS	13 days	Fri 6/7/19	Tue 6/25/19																							
36		REMOVE PCCP, SIDWALK, CURB	2 days	Fri 6/7/19	Mon 6/10/19	33																						
37		EXCAVATON AND EMBANKMENT	5 days	Tue 6/11/19	Mon 6/17/19	36																						

Critical		Split		Finish-only		Baseline Milestone		Manual Summary		Inactive Task	
Critical Split		Task Progress		Duration-only		Milestone		Project Summary		Inactive Milestone	
Critical Progress		Manual Task		Baseline		Summary Progress		External Tasks		Inactive Summary	
Task		Start-only		Baseline Split		Summary		External Milestone		Deadline	


AREO WESTBOW ROUNDABOUT

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	8, '19							May 5, '19							May 12, '19							May 19,
								M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	
38	🚀	DRAINAGE	2 days	Tue 6/18/19	Wed 6/19/19	37																							
39	🚀	FINISH SUB GRADE	2 days	Thu 6/20/19	Fri 6/21/19	38																							
40	🚀	CSBC	2 days	Mon 6/24/19	Tue 6/25/19	39																							
41	🏠	POWER CITY	5 days	Tue 6/18/19	Mon 6/24/19																								
42	🚀	ELECTRICAL	5 days	Tue 6/18/19	Mon 6/24/19	37																							
43	🏠	FIVE STAR	3 days	Wed 6/26/19	Fri 6/28/19																								
44	🚀	CURB AND SIDEWALK	3 days	Wed 6/26/19	Fri 6/28/19	40																							
45	🏠	STRIPE RITE	1 day	Mon 7/8/19	Mon 7/8/19																								
46	🚀	TEMP STRIPE FOR PHASE 3	1 day	Mon 7/8/19	Mon 7/8/19	34																							
47	🏠	PHASE 3	22 days	Tue 7/9/19	Wed 8/7/19																								
48	🏠	ACME	22 days	Tue 7/9/19	Wed 8/7/19																								
49	🚀	SAW CUT AND BREAK PCCP	2 days	Tue 7/9/19	Wed 7/10/19	46																							
50	🚀	PCCP	5 days	Thu 8/1/19	Wed 8/7/19	60																							
51	🏠	MURPHY BROTHERS	12 days	Thu 7/11/19	Fri 7/26/19																								
52	🚀	REMOVE PCCP, SIDEWALK, CURB	2 days	Thu 7/11/19	Fri 7/12/19	49																							
53	🚀	EXCAVATON AND EMBANKMENT	4 days	Mon 7/15/19	Thu 7/18/19	52																							
54	🚀	DRAINAGE	2 days	Fri 7/19/19	Mon 7/22/19	53																							
55	🚀	FINISH SUB GRADE	2 days	Tue 7/23/19	Wed 7/24/19	54																							
56	🚀	CSBC	2 days	Thu 7/25/19	Fri 7/26/19	55																							
57	🏠	POWER CITY	5 days	Mon 7/15/19	Fri 7/19/19																								
58	🚀	ELECTRICAL	5 days	Mon 7/15/19	Fri 7/19/19	52																							
59	🏠	FIVE STAR	3 days	Mon 7/29/19	Wed 7/31/19																								
60	🚀	CURB AND SIDEWALK	3 days	Mon 7/29/19	Wed 7/31/19	56																							
61	🏠	PHASE 4	21 days	Mon 7/29/19	Mon 8/26/19																								
62	🏠	ACME	5 days	Mon 7/29/19	Fri 8/2/19																								
63	🚀	SEED AND SOD	5 days	Mon 7/29/19	Fri 8/2/19	56																							
64	🏠	FIVE STAR	6 days	Thu 8/8/19	Thu 8/15/19																								
65	🚀	CURB FOR ISLAND	3 days	Thu 8/8/19	Mon 8/12/19	50																							
66	🚀	ISLAND TREATMENT	3 days	Tue 8/13/19	Thu 8/15/19	65																							
67	🏠	POWER CITY	7 days	Thu 8/1/19	Fri 8/9/19																								
68	🚀	FINISH ELECTRICAL	7 days	Thu 8/1/19	Fri 8/9/19	60																							
69	🚀	INSTALL LUMINARE	7 days	Thu 8/1/19	Fri 8/9/19	60,4																							
70	🏠	STRIPE RITE	7 days	Fri 8/16/19	Mon 8/26/19																								
71	🚀	PERMENANT STRIPE	7 days	Fri 8/16/19	Mon 8/26/19	66																							
72	🚀	SIGNS	7 days	Fri 8/16/19	Mon 8/26/19	66																							

Critical		Split		Finish-only		Baseline Milestone		Manual Summary		Inactive Task	
Critical Split		Task Progress		Duration-only		Milestone		Project Summary		Inactive Milestone	
Critical Progress		Manual Task		Baseline		Summary Progress		External Tasks		Inactive Summary	
Task		Start-only		Baseline Split		Summary		External Milestone		Deadline	


AREO WESTBOW ROUNDABOUT

19, '19 May 26, '19 Jun 2, '19 Jun 9, '19 Jun 16, '19 Jun 23, '19 Jun 30, '19 Jul 7, '19
M | T | W | T | F | S S | M | T | W | T | F | S S | M | T | W | T | F | S S | M | T | W | T | F | S S | M | T | W | T | F | S S | M | T | W | T | F | S S | M | T | W | T | F | S S | M | T | W | T | F | S

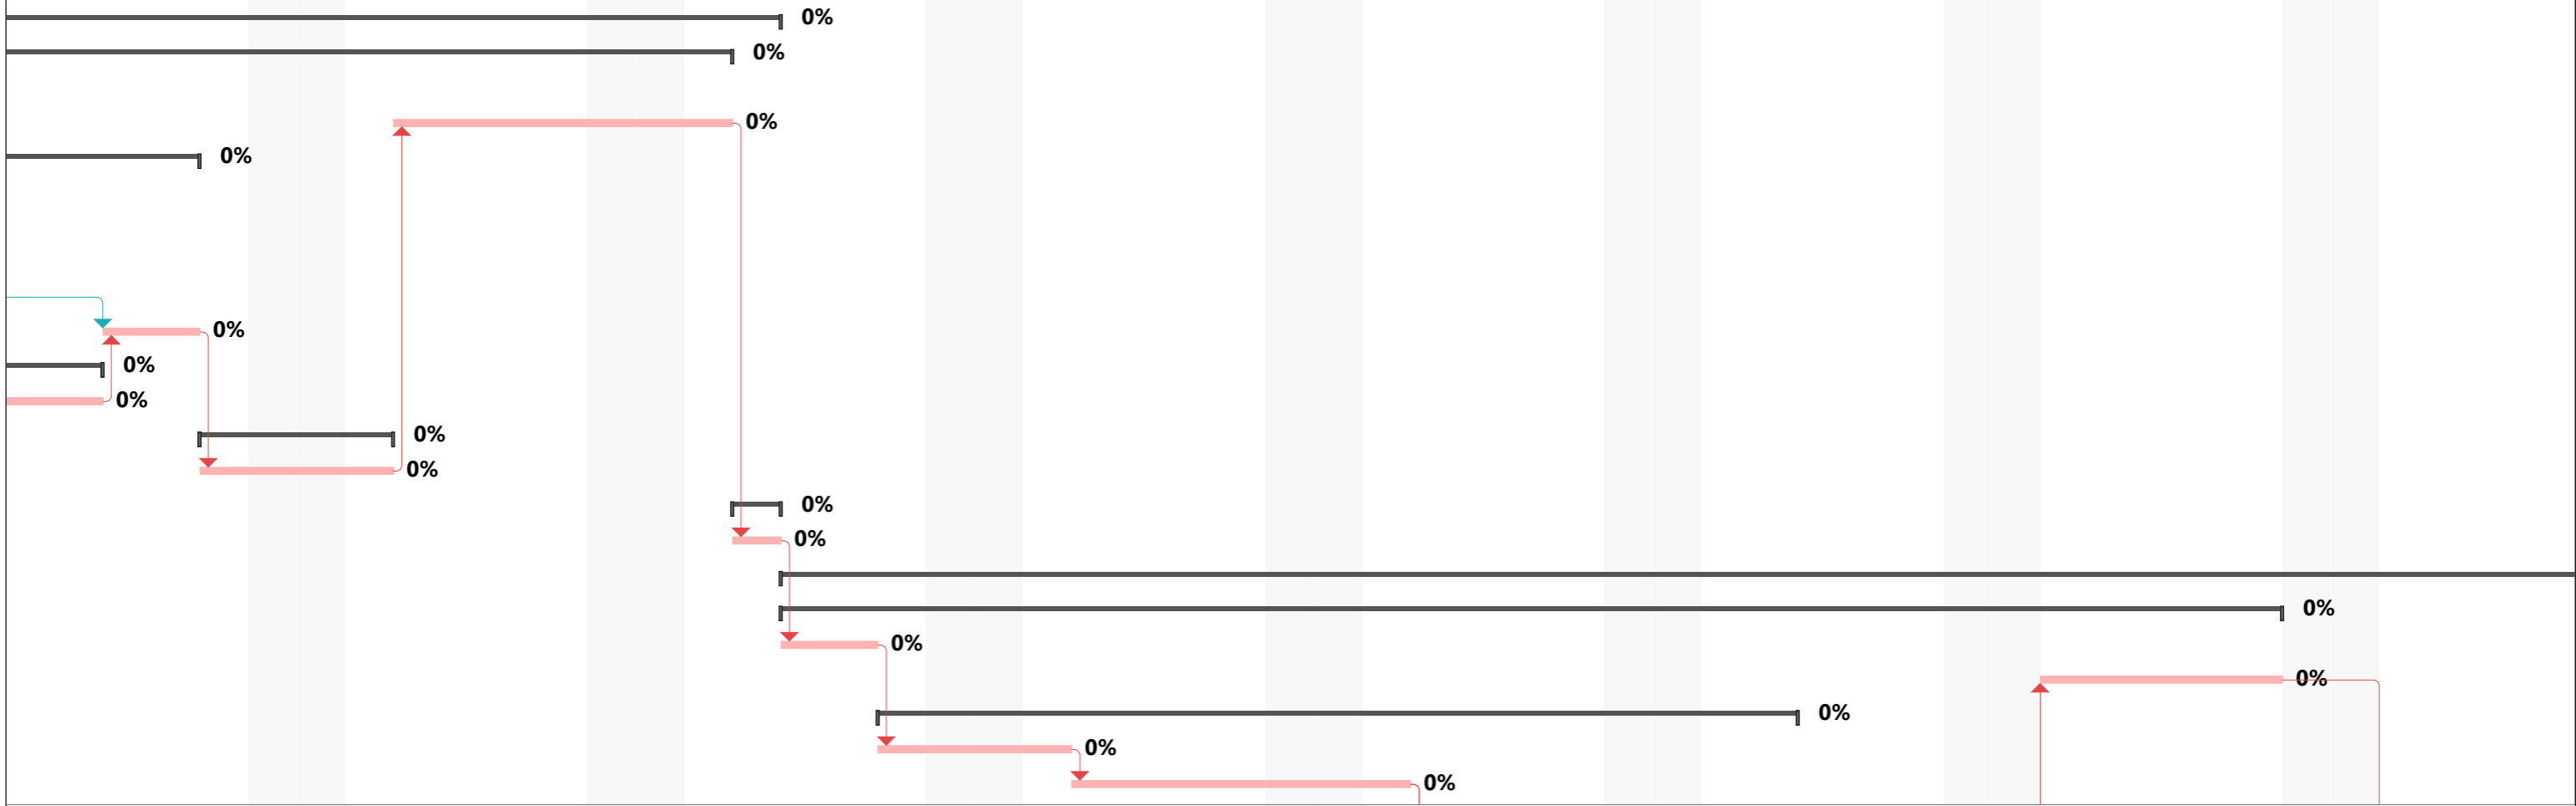


Critical		Split		Finish-only		Baseline Milestone		Manual Summary		Inactive Task	
Critical Split		Task Progress		Duration-only		Milestone		Project Summary		Inactive Milestone	
Critical Progress		Manual Task		Baseline		Summary Progress		External Tasks		Inactive Summary	
Task		Start-only		Baseline Split		Summary		External Milestone		Deadline	

AREO WESTBOW ROUNDABOUT

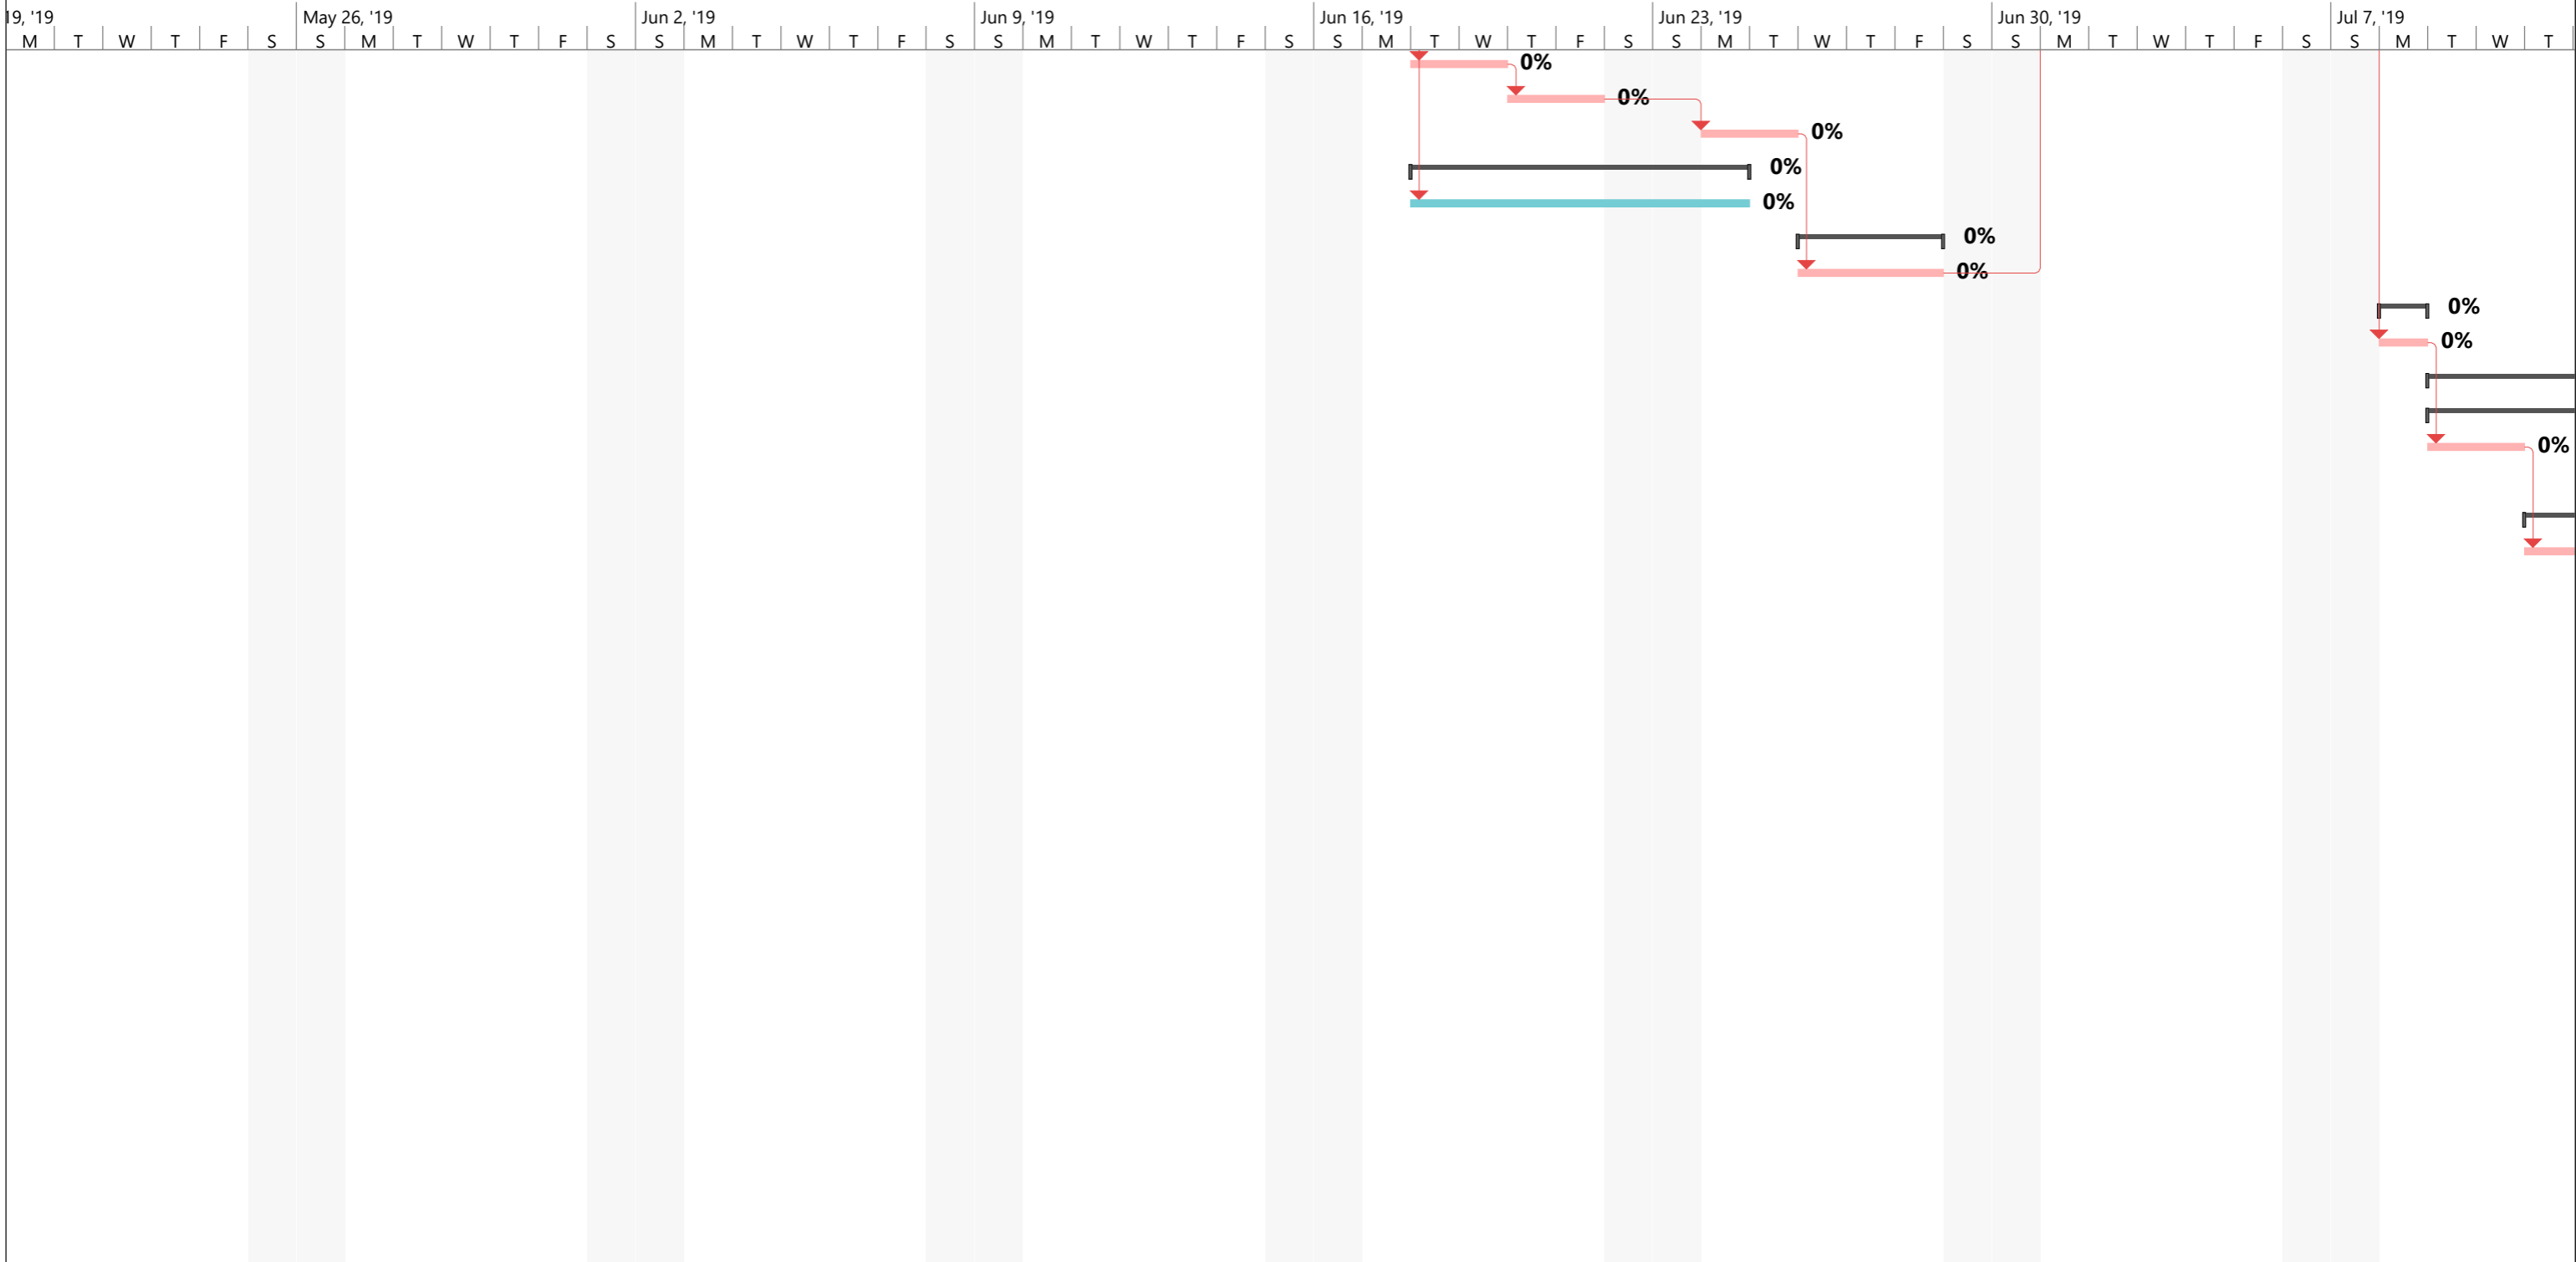

Critical		Split		Finish-only		Baseline Milestone		Manual Summary		Inactive Task	
Critical Split		Task Progress		Duration-only		Milestone		Project Summary		Inactive Milestone	
Critical Progress		Manual Task		Baseline		Summary Progress		External Tasks		Inactive Summary	
Task		Start-only		Baseline Split		Summary		External Milestone		Deadline	

AREO WESTBOW ROUNDABOUT

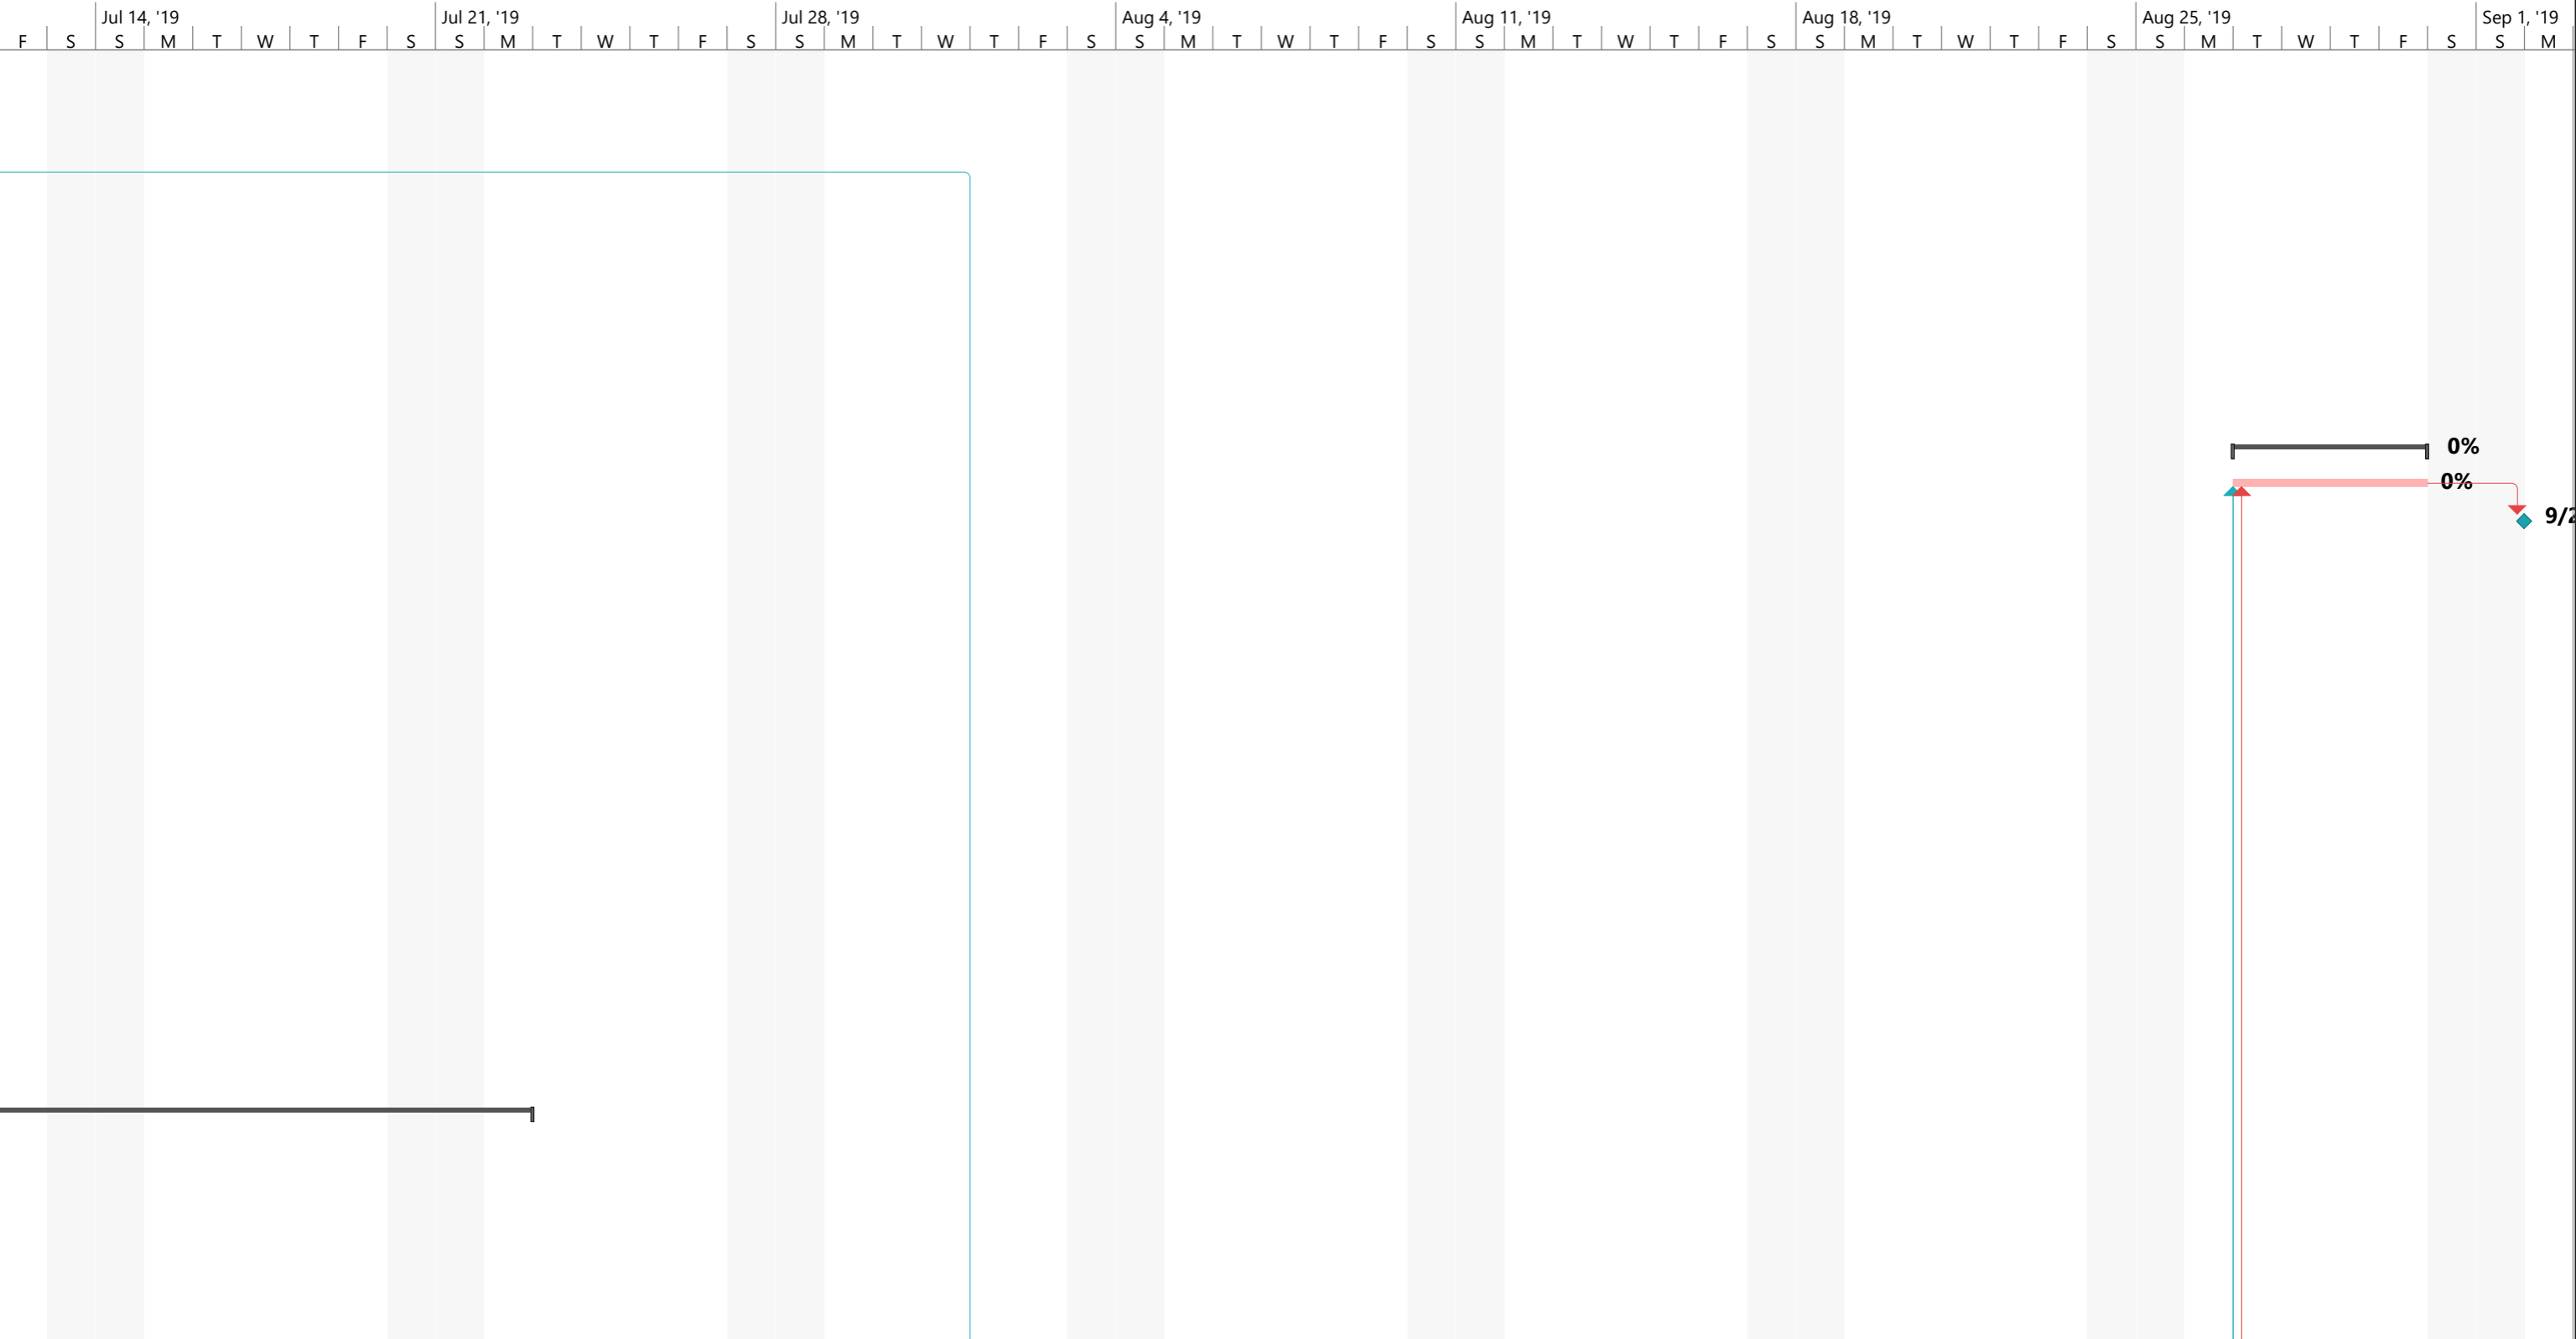

Critical		Split		Finish-only		Baseline Milestone		Manual Summary		Inactive Task	
Critical Split		Task Progress		Duration-only		Milestone		Project Summary		Inactive Milestone	
Critical Progress		Manual Task		Baseline		Summary Progress		External Tasks		Inactive Summary	
Task		Start-only		Baseline Split		Summary		External Milestone		Deadline	

